




Olympia Transit Center Expansion - Update

March 6, 2019

OTC Project Update

- **Quick update on Progress**
- **Schedule and budget**
- **Highlights**

OTC Site Plan

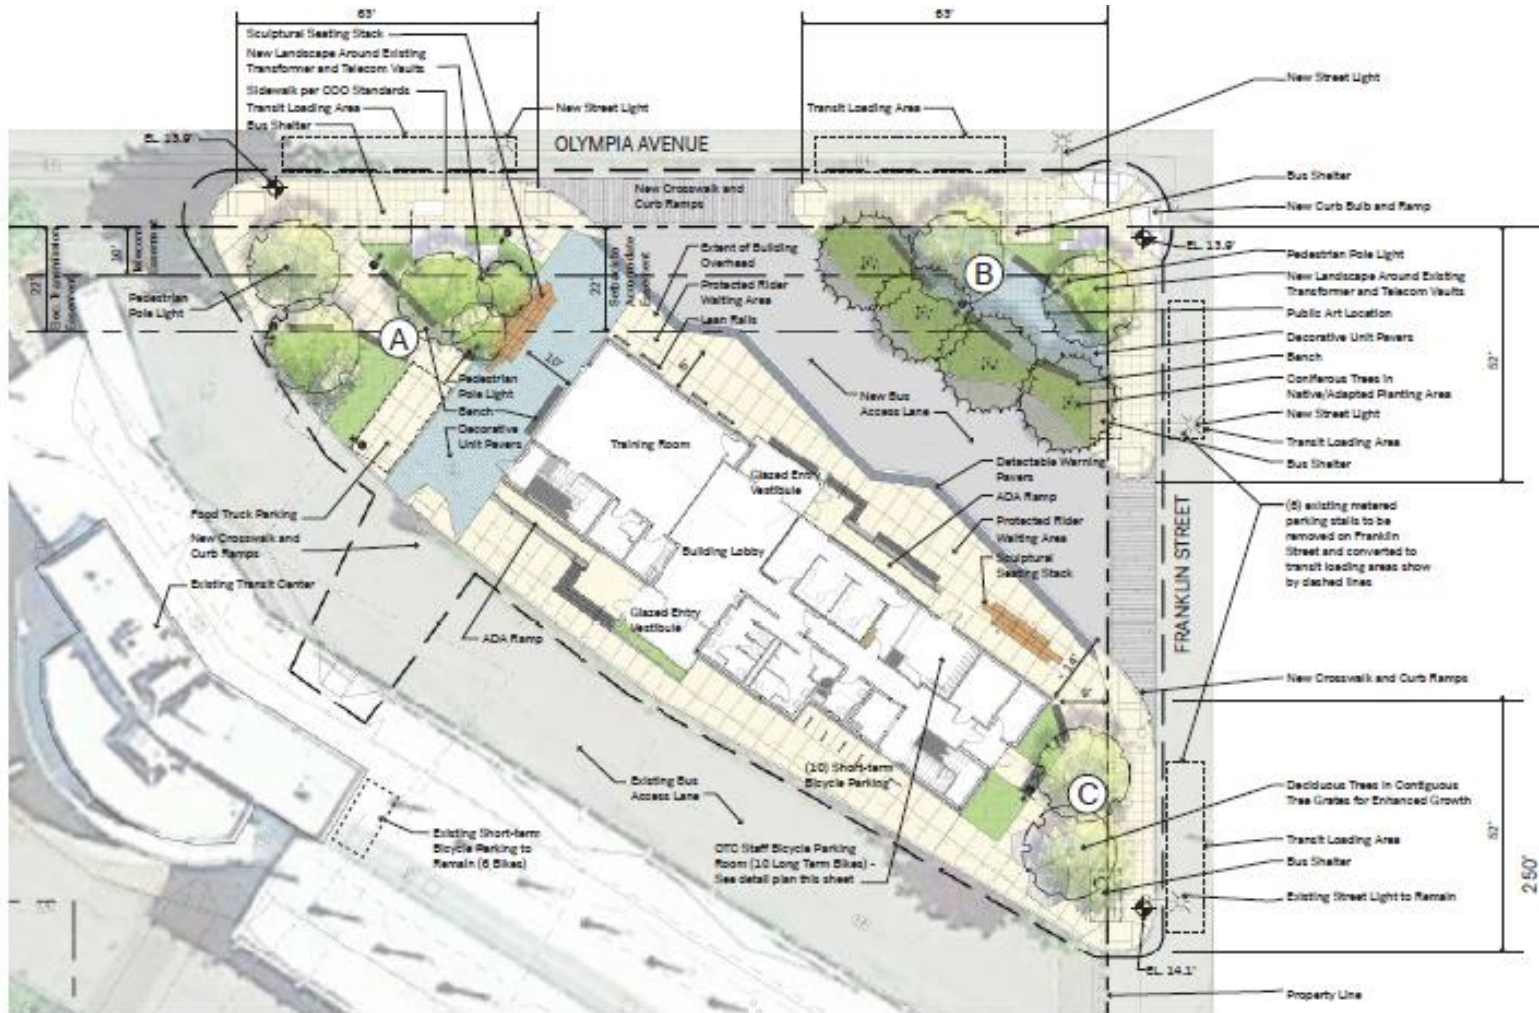

Project Status

- Contract Awarded to Graham in October 2018 – (\$8.7 million)
- Construction NTP issued Nov. 7, 2018
- Site mobilization and work onsite started on Nov. 21, 2018
- Currently about 2-3 weeks behind schedule
 - Soil/foundation/geotechnical
 - weather

OTC Site – November 30, 2018



OTC Site – Delays / Soils



12/12/2018

Building the SOG



12/13/2018

Building the SOG



12/14/2018

Building the SOG



12/17/2018

Building the SOG



12/18/2018

Building the SOG



1/2/2019

Building the SOG



1/21/2019

Building the SOG



1/30/2019

Building the SOG



2/08/2019

OTC Site – Delays / Weather



2/11/2019

Building the SOG



2/20/2019

Building the SOG



2/21/2019

[dot-file\otcCamera](#)

INTERcity
TRANSIT

Feb 21, 2019 -The Big Pour



12/12/2018

OTC Site – March 4, 2019



Project Status

90 days into construction....

- Slab-on-grade - Foundation complete
- Building will go vertical by about March 20th.
 - Steel support structures will go up quickly
 - Followed by second floor and internal framing
 - Critical path items now follow schedule and order of subs and work flow.

Schedule & Budget

90 days into construction....

- Just over \$2 million expended since NTP
- Have received \$1.6 M reimbursement from FTA
- Remaining FTA funds to draw on \$2.6M
- Have some C/O costs related to soil stabilization, elevator pit sump, some small changes. Total less than \$50k
- Still expected to be complete on schedule by November 2019.
- Planning for revision of Route/Bay assignments
- Still Waiting on Agreement from Greyhound

Questions?

